



April 21, 2022

Sauganash Elementary School Annex and Renovations - Project #05425

Status: Construction - Weekly Report

1. Key Dates:

- Notice of Award: 11.18.21*
- Notice to Proceed: 12.03.21*
- Milestone #1 (utility work, site demolition, and UST removal): 12.31.21*
- Milestone #2 (interior renovations and mechanical upgrades): 08.05.22
- Substantial Completion (gym demolition and new annex): 11.30.22

2. Construction Progress – Completion Percentages:

- Milestone #1: 100%
- Milestone #2: 14%
- Substantial Completion: 15%

3. Completed Activities:

- ERS installation
- ERS equipment demobilization
- New foundations and grade beam layout and controls
- Removal and salvage of glazed block at existing school

4. On-Going Activities:

- Construction submittals and material procurement
- Pre-submittal review meetings (various trades)
- Generator maintenance
- Site control maintenance
- Interior and exterior air monitoring
- Seismograph monitoring
- New basement and foundation excavation
- Excavation material haul-off
- Street cleaning

5. Upcoming Activities (April 22nd through April 28th):

- Pre-Installation Conferences (fire proofing, windows/storefront, and roofing)
- New basement and foundation excavation
- Excavation material haul-off

6. Working Days and Hours (April 22nd through April 28th):

- Friday (April 22nd): 6:00am to 9:00pm
- Saturday (April 23rd): No work
- Sunday (April 24th): No Work
- Monday (April 25th) through Thursday (April 28th): 6:00am to 9:00pm

Note: No work anticipated on April 23rd and April 24th.


7. Current Construction Progress Photographs:

- Attached

Notes: *actual dates; **approved revised completion dates



Earth Retention System installation

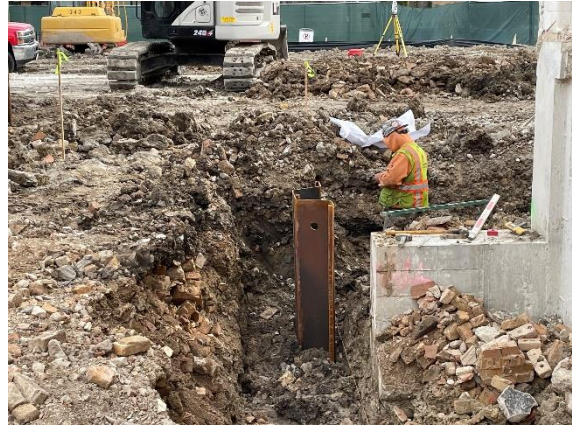

Earth Retention System installation



New basement excavation



Excavation material haul-off



Existing glazed block removal and salvage



Removal of salvaged glazed block
