



September 22, 2022

## Sauganash Elementary School Annex and Renovations - Project #05425

Status: Construction - Weekly Report

### 1. Key Dates:

- Notice of Award: 11.18.21\*
- Notice to Proceed: 12.03.21\*
- Milestone #1 (utility work, site demolition, and UST removal): 12.31.21\*
- Milestone #2 (interior renovations and mechanical upgrades): 08.05.22
- Substantial Completion (gym demolition and new annex): 11.30.22

### 2. Construction Progress – Completion Percentages:

- Milestone #1: 100%
- Milestone #2: 99%
- Substantial Completion: 41%

### 3. Completed Activities:

- Bio-Foam at elevator pit
- Waterproofing at West elevation (foundation wall)
- Engineered fill at West elevation
- StormTrap installation
- Epoxy flooring (existing school basement)

### 4. On-Going Activities:

- Construction submittals, material procurement, and pre-submittal review meetings (various trades)
- Site control maintenance
- Street cleaning
- Seismograph monitoring
- Rebar inspections by City (on-going)
- Construction mock-ups (masonry, roofing, concrete slab, wall system, and window/door openings)
- Ground-level caisson cap and grade beam installation
- Upper-level rebar installation

### 5. Upcoming Activities (September 23<sup>rd</sup> through September 29<sup>th</sup>):

- Concrete for mechanical pads at first floor mechanical room
- Storm Trap drainage piping
- Elevator pit wall framing
- Lower-level temporary lighting
- Concrete curb at StormTrap

### 6. Working Days and Hours (September 23<sup>rd</sup> through September 29<sup>th</sup>):

- Friday (September 23<sup>rd</sup>): 6:00am to 9:00pm
- Saturday (September 24<sup>th</sup>): 7:00am to 5:00pm
- Sunday (September 25<sup>th</sup>): 8:00am to 5:00pm
- Monday (September 26<sup>th</sup>) through Thursday (September 29<sup>th</sup>): 6:00am to 9:00pm

**Note:** Foundation work anticipated on September 24<sup>th</sup>, and September 25<sup>th</sup>, pending favorable weather conditions.

### 7. Current Construction Progress Photographs:

- Attached


Notes: \*actual date(s); \*\*approved revised completion date(s); \*\*\*current projected Milestone and SC date(s)



Framing at grade beam #1



New light fixtures at existing classroom room #101

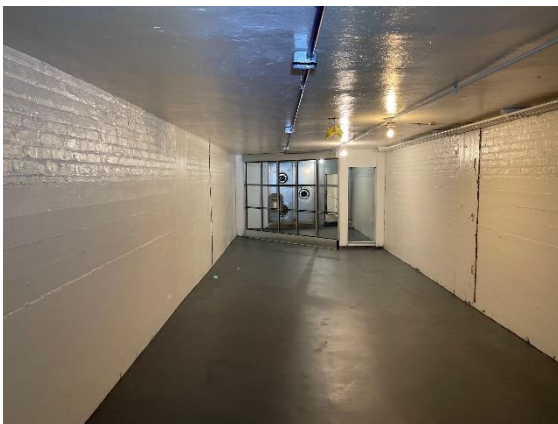

Epoxy flooring at air tunnel (existing school)



Storm Trap System
